

جامعة ابن طفيل
Ibn Tofaïl University

Faculté des Sciences
Kénitra, Maroc

Gestion de Projet

CYCLE DE VIE

Présenté par :

Mohamed AMNAI

01/10/2025

PLAN

1. INTRODUCTION
2. CYCLE DE VIE D'UN PROJET PRÉDICTIF
3. CYCLE DE VIE D'UN PROJET AGILE
4. LIVRABLES PROJETS AGILE VS PRÉDICTIF
5. CONCEPTS


1. INTRODUCTION



• **Business lifecycle** addresses the overall organizational trajectory while the product lifecycle hones in on specific offerings, and the project lifecycle pertains to temporary endeavors with defined goals in order to develop specific product or services.

Il permet de comprendre comment évoluent sa **stratégie, sa structure, ses ressources et sa performance** au fil du temps.

1. INTRODUCTION




• **Business lifecycle** addresses the overall organizational trajectory while the product lifecycle hones in on specific offerings, and the project lifecycle pertains to temporary endeavors with defined goals in order to develop specific product or services.

• **Product lifecycle** focuses on the journey of a specific product from development and introduction to market. Stages commonly include introduction, growth, maturity, and decline.

Il décrit l'évolution de sa **performance commerciale**, de sa **rentabilité** et de sa **position concurrentielle** au fil du temps.

1. INTRODUCTION

Université Ibn Tofail
Faculté des Sciences

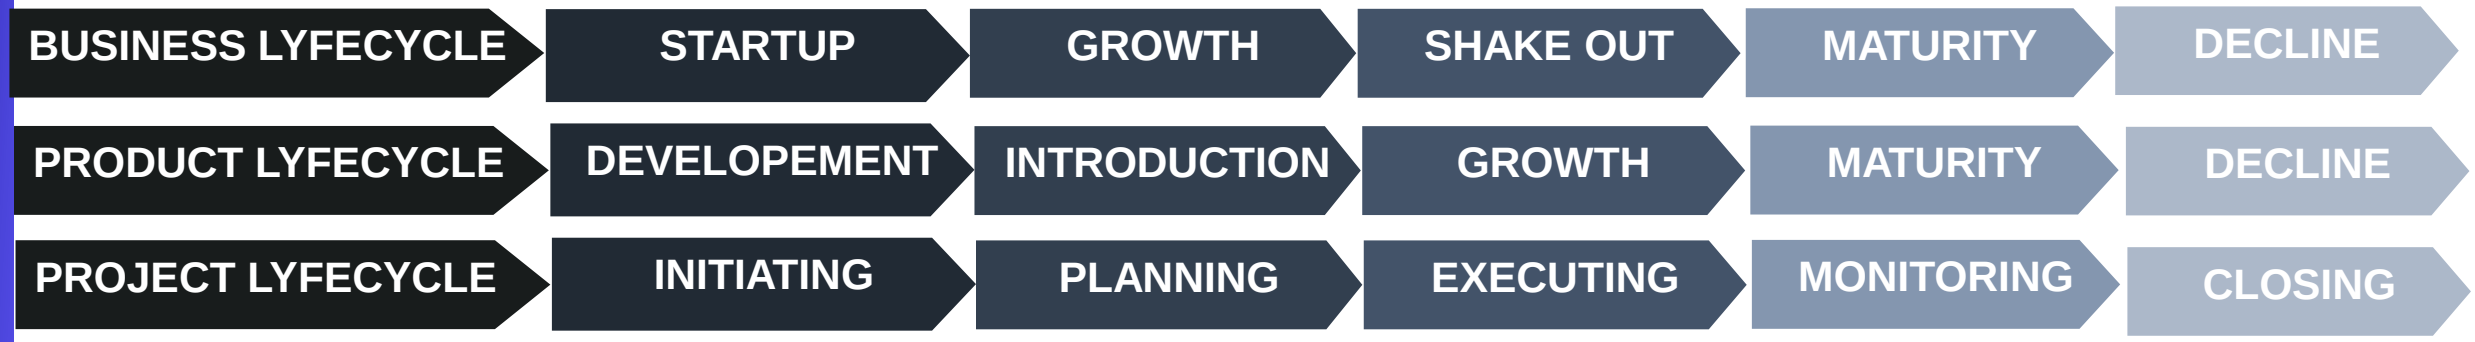

• **Business lifecycle** addresses the overall organizational trajectory while the product lifecycle hones in on specific offerings, and the project lifecycle pertains to temporary endeavors with defined goals in order to develop specific product or services.

• **Product lifecycle** focuses on the journey of a specific product from development and introduction to market. Stages commonly include introduction, growth, maturity, and decline.

• **Project lifecycle** is concerned with the phases a project passes through from initiation to completion. Common stages encompass initiation, planning, execution, monitoring/controlling, and closure.

Date

2. CYCLE DE VIE PROJET PRÉDICTIF

Présenté par :


2. CYCLE DE VIE PROJET PREDICTIF

INITIATING


POJECT Baseline

•**Baseline** = Ensemble des plans approuvés pour le **périmètre**, le **calendrier** et le **budget** du projet, utilisé pour comparer les résultats réels aux prévisions et mesurer la performance.
•Elle représente **“le contrat interne de référence”** entre le **chef de projet**, les **parties prenantes** et le **sponsor**.

2. CYCLE DE VIE PROJET PREDICTIF

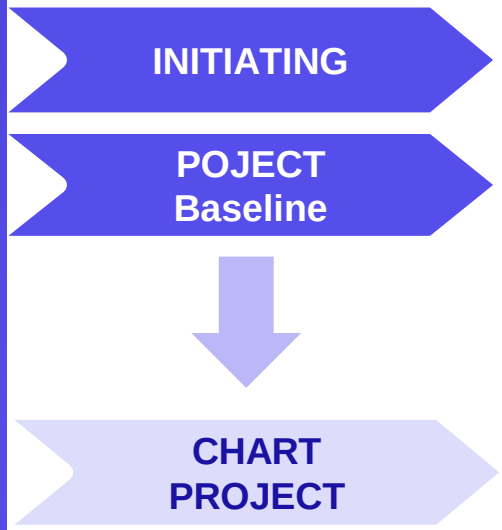


2. CYCLE DE VIE PROJET PREDICTIF




•Le **Project Management Plan (PMP)** — ou **Plan de Management du Projet** — est **le document de référence principal** dans un projet à **cycle de vie prédictif** (*Waterfall*).
•C'est **le plan directeur** qui décrit **comment** le projet sera exécuté, surveillé, contrôlé et clôturé
•Il décret les **stratégies** d'exécution du projet


2. CYCLE DE VIE PROJET PREDICTIF

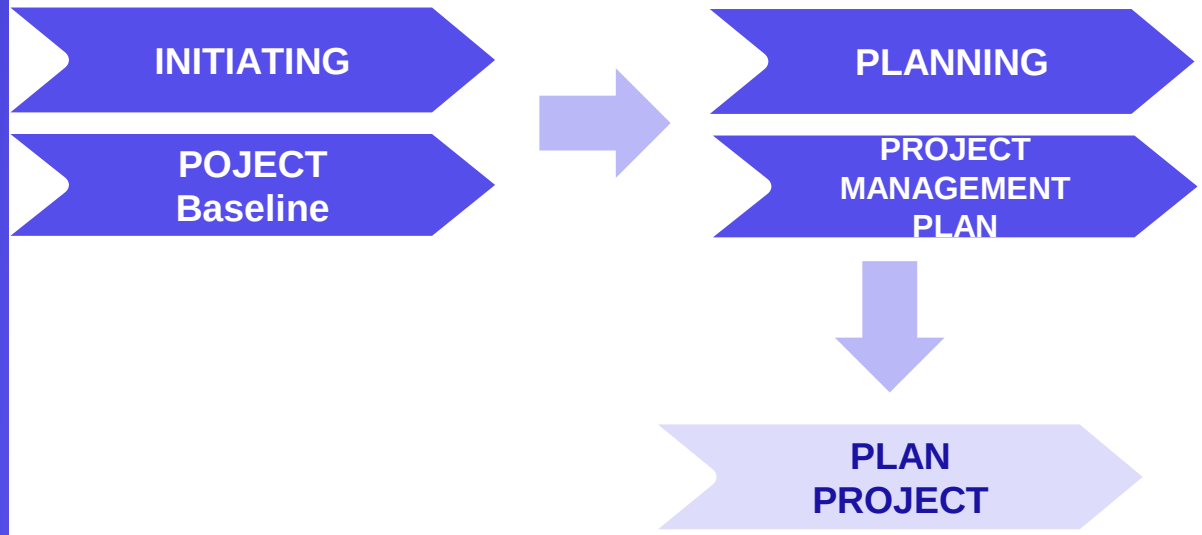


2. CYCLE DE VIE PROJET PREDICTIF

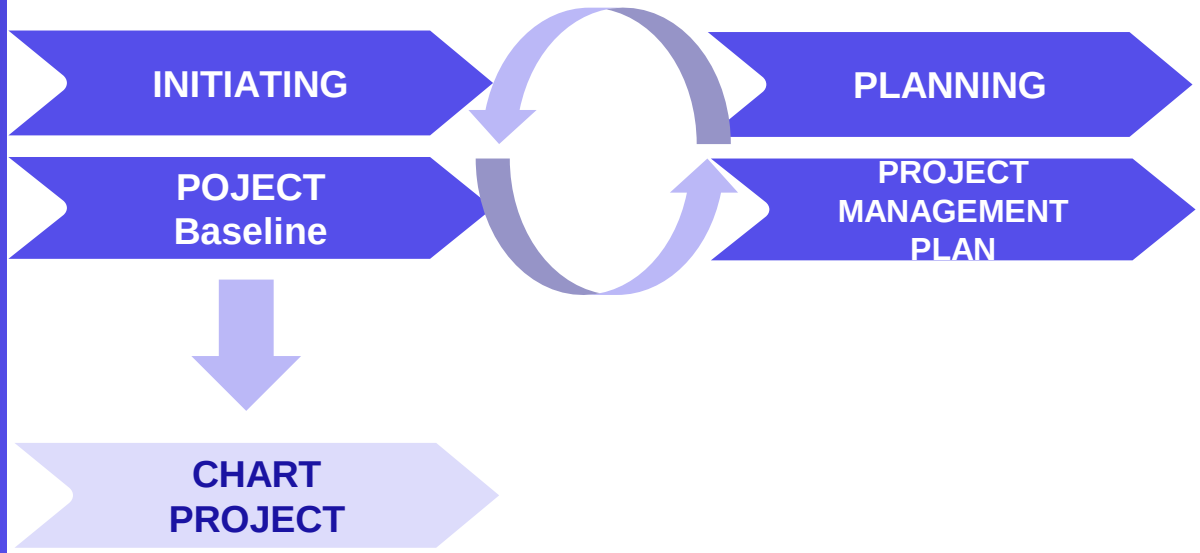


2. CYCLE DE VIE PROJET PREDICTIF

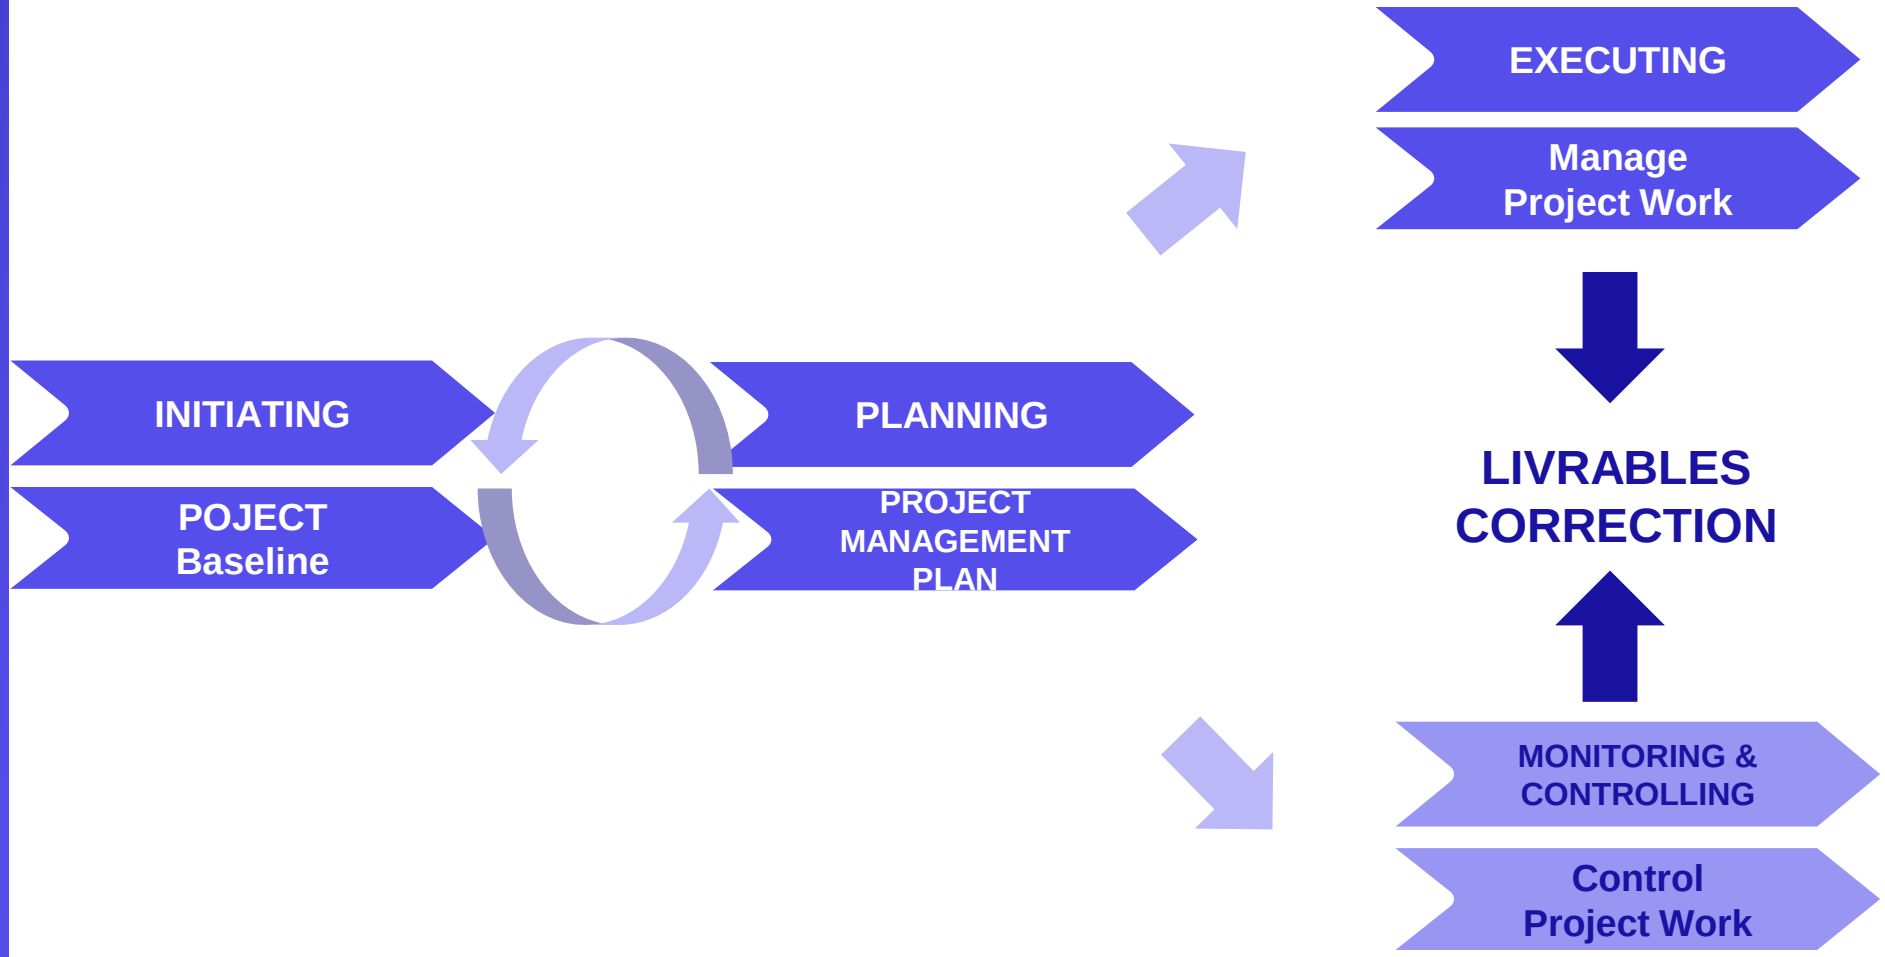


2. CYCLE DE VIE PROJET PREDICTIF

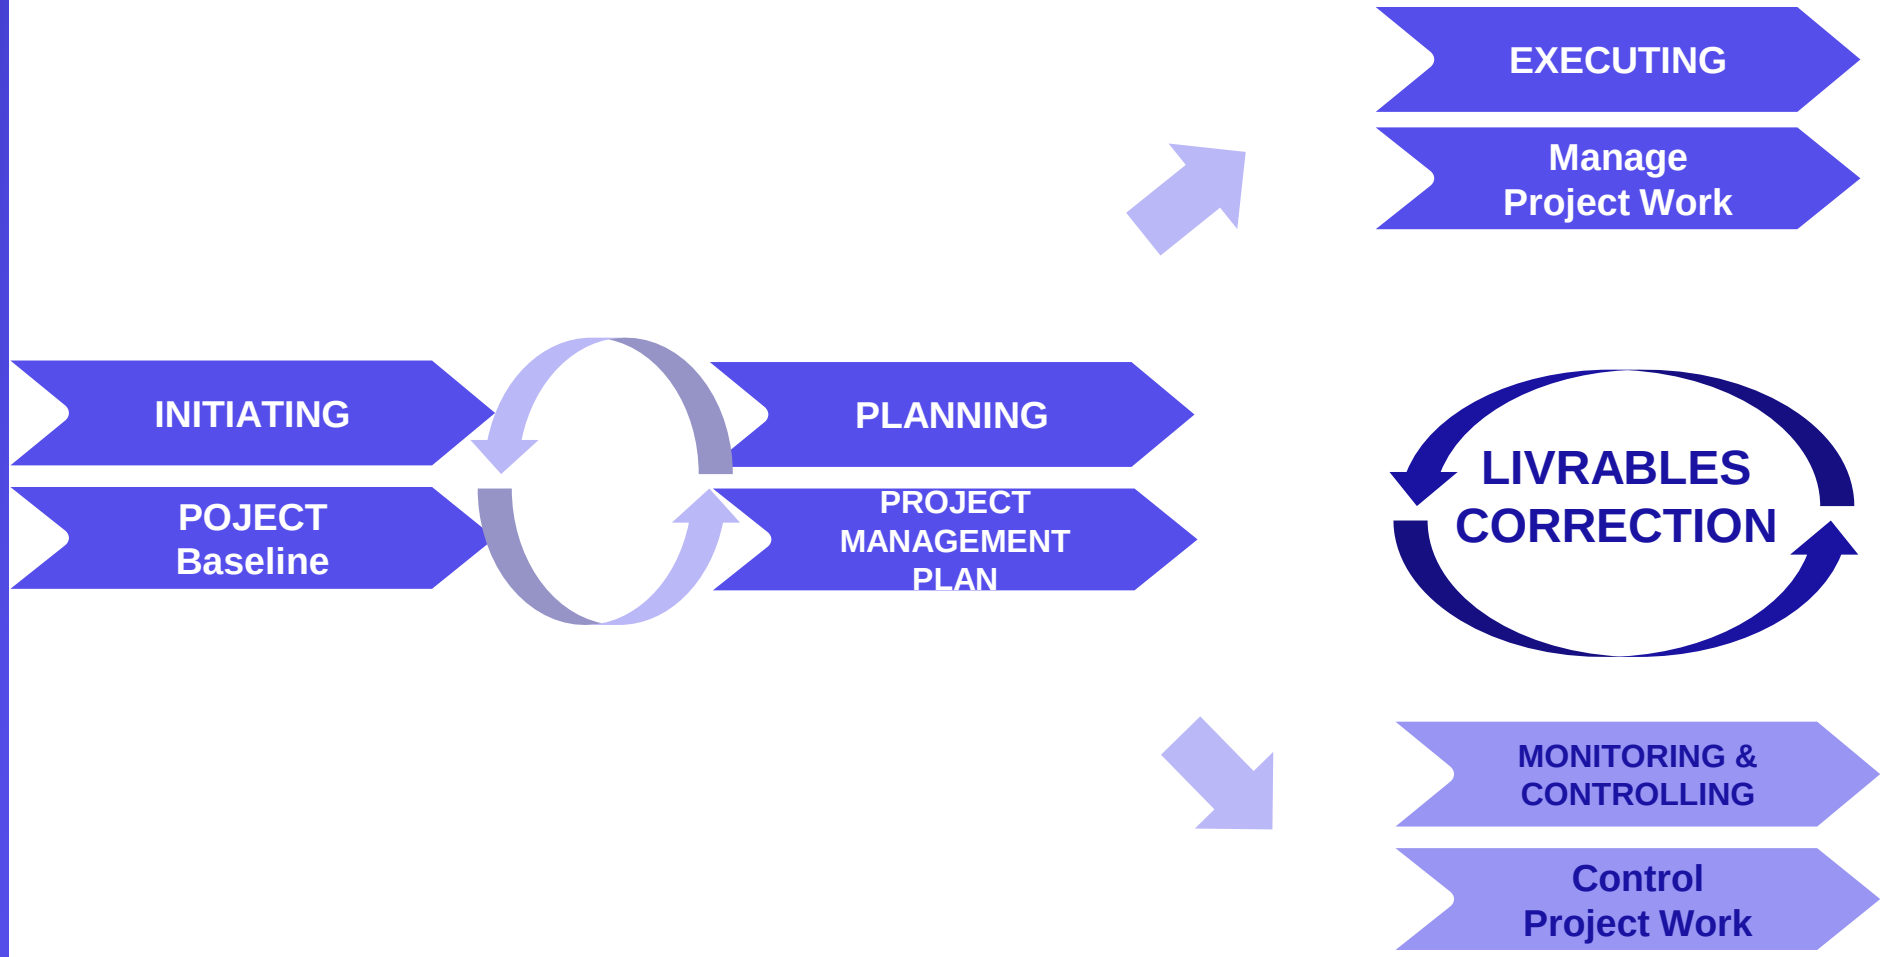

2. CYCLE DE VIE PROJET PREDICTIF

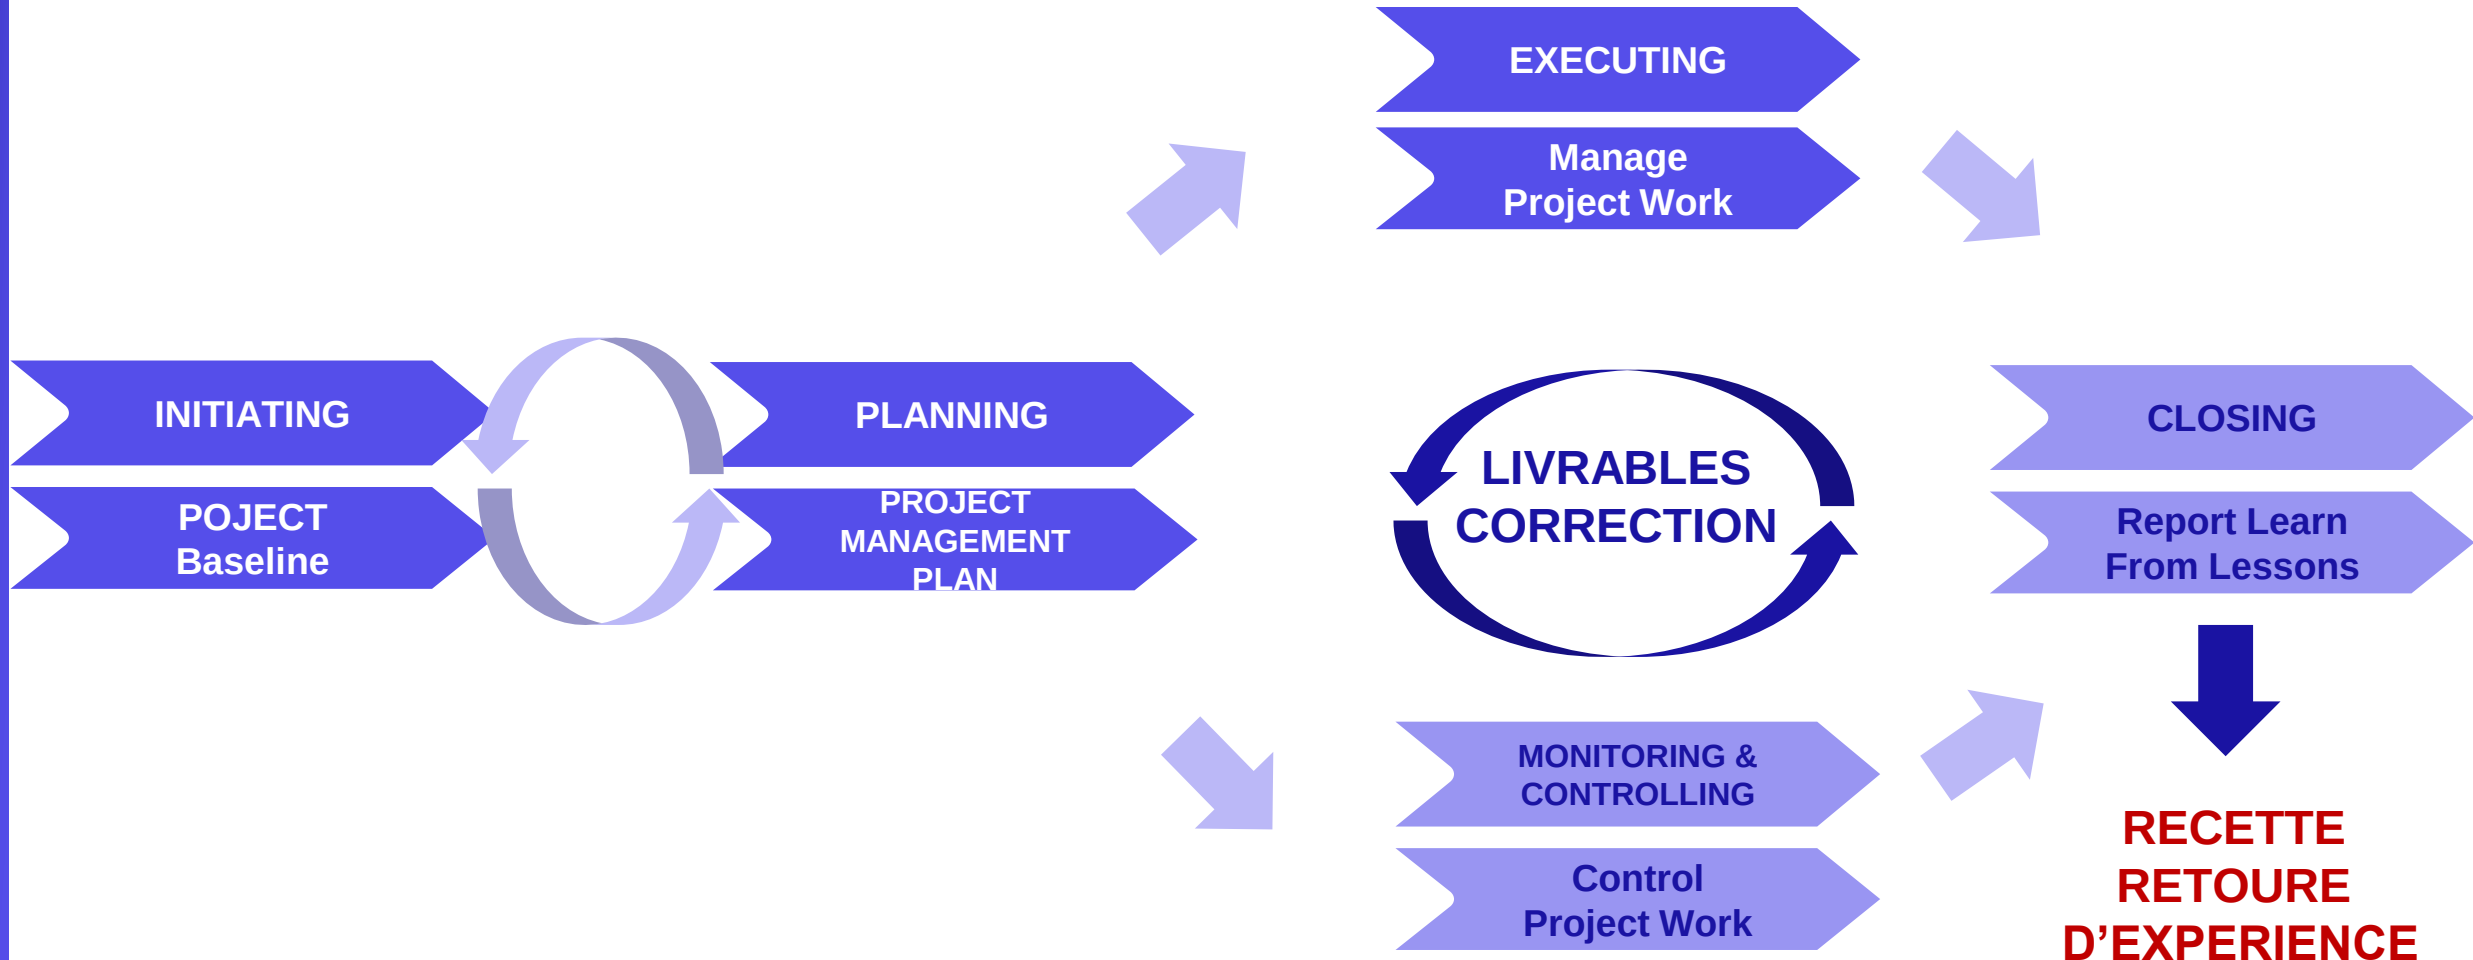

2. CYCLE DE VIE PROJET PREDICTIF

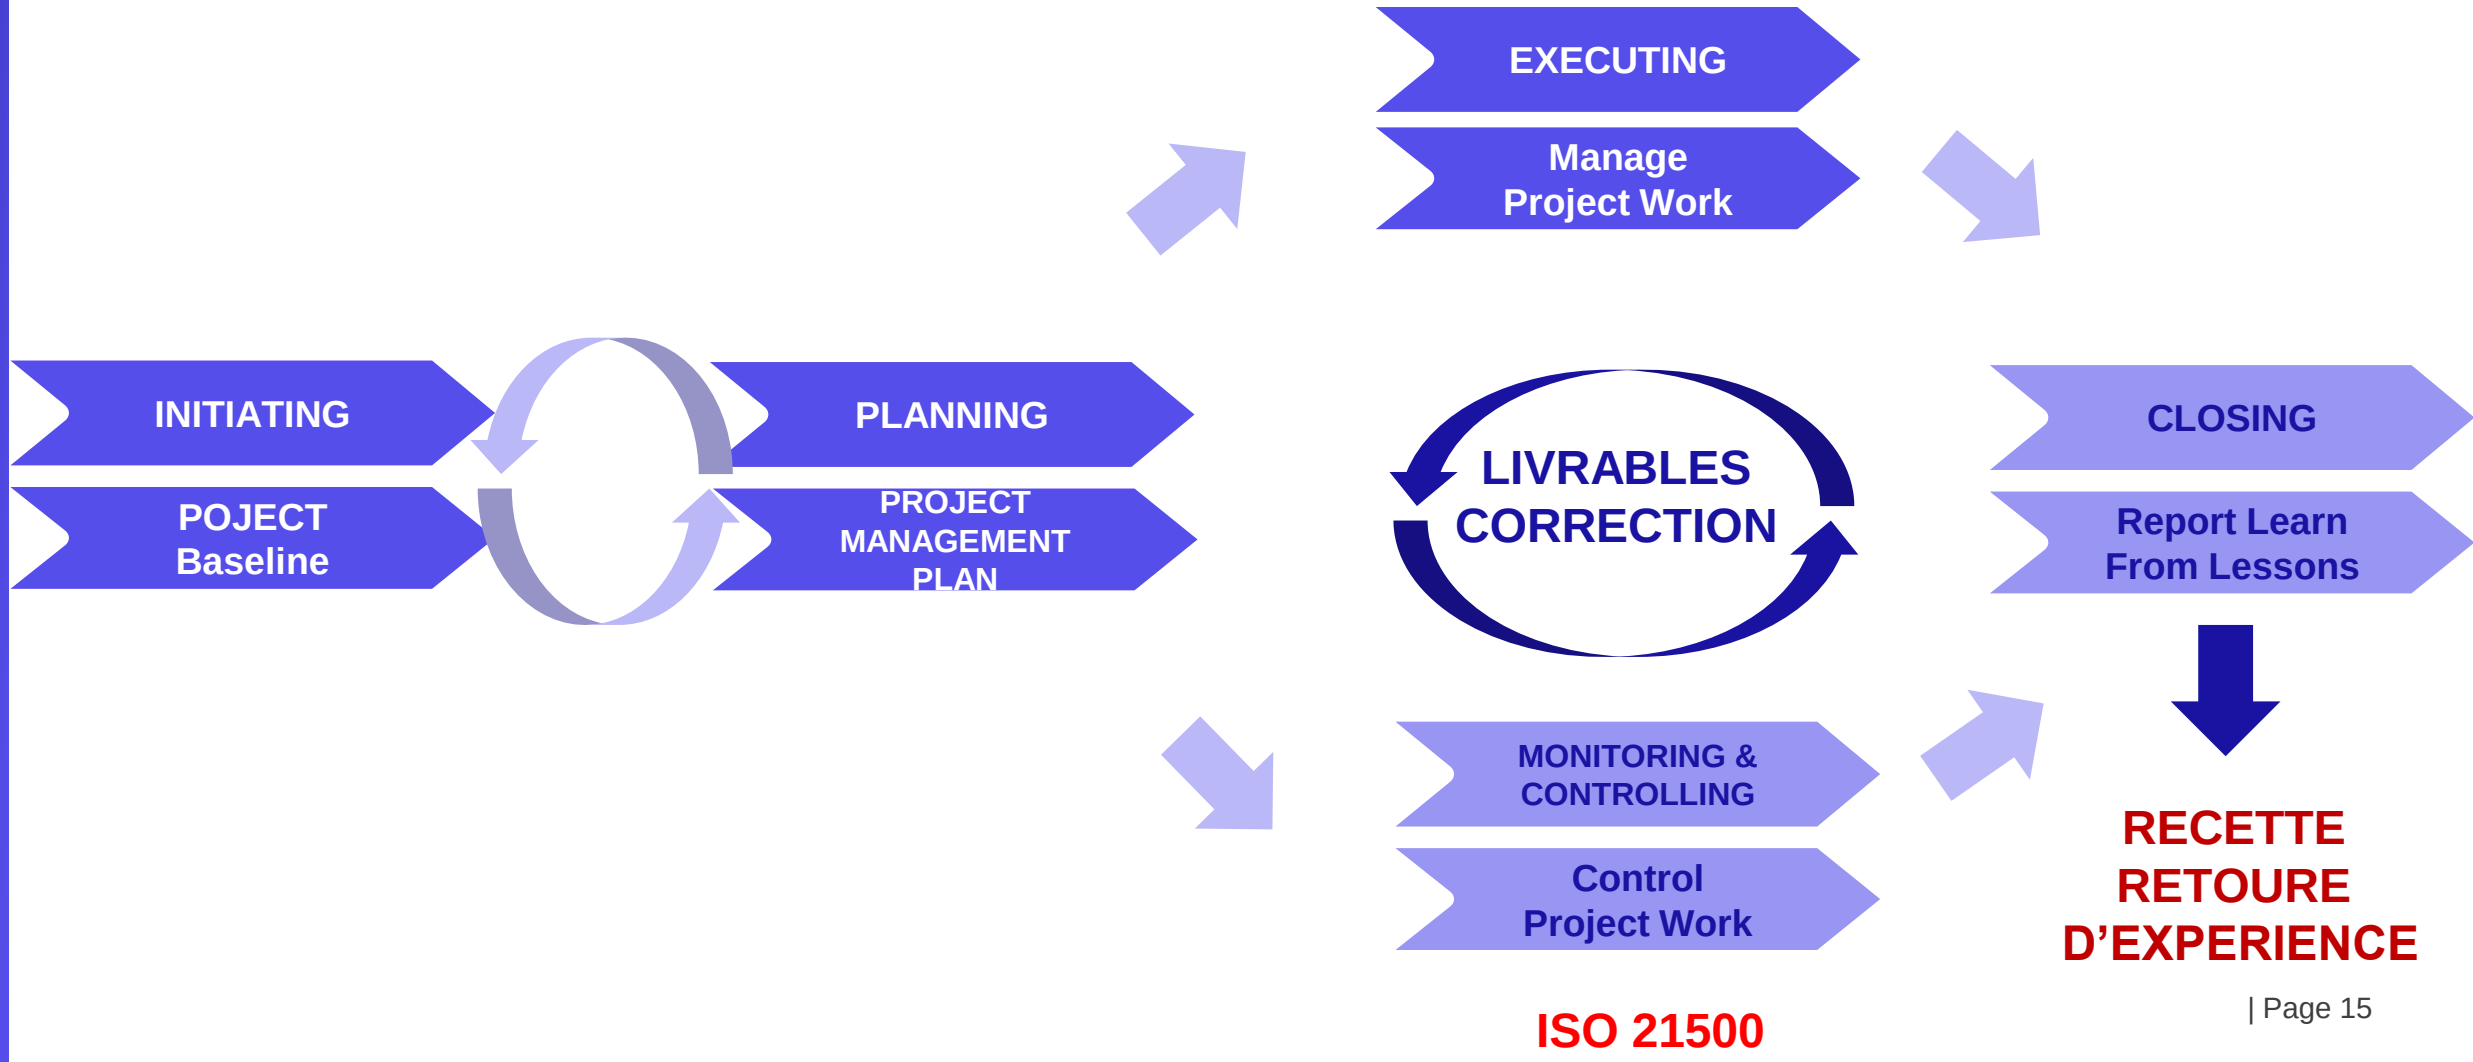

Date

3. CYCLE DE VIE PROJET AGILE

Présenté par :


3. CYCLE DE VIE PROJET AGILE

BACKLOG


PRODUCT

•Le **product backlog** représente la **liste priorisée** de toutes les **fonctionnalités, exigences et tâches** nécessaires à la **création du produit ou service**.
•Il est **évolutif** et **sert de référence** pour planifier et suivre l'exécution du projet.


3. CYCLE DE VIE PROJET AGILE

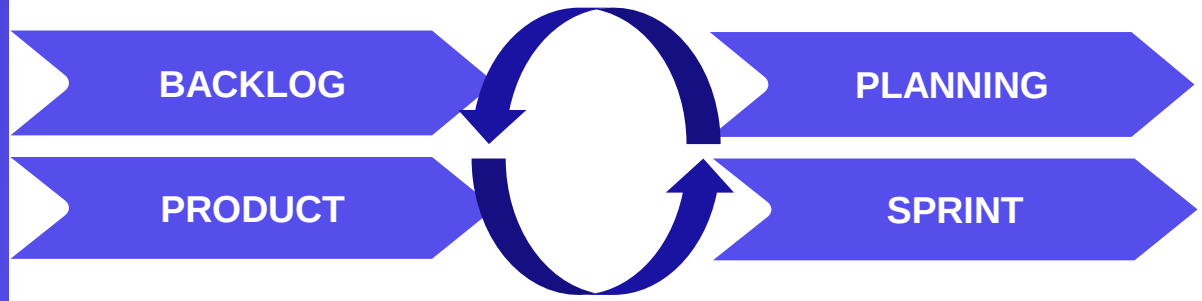


3. CYCLE DE VIE PROJET AGILE

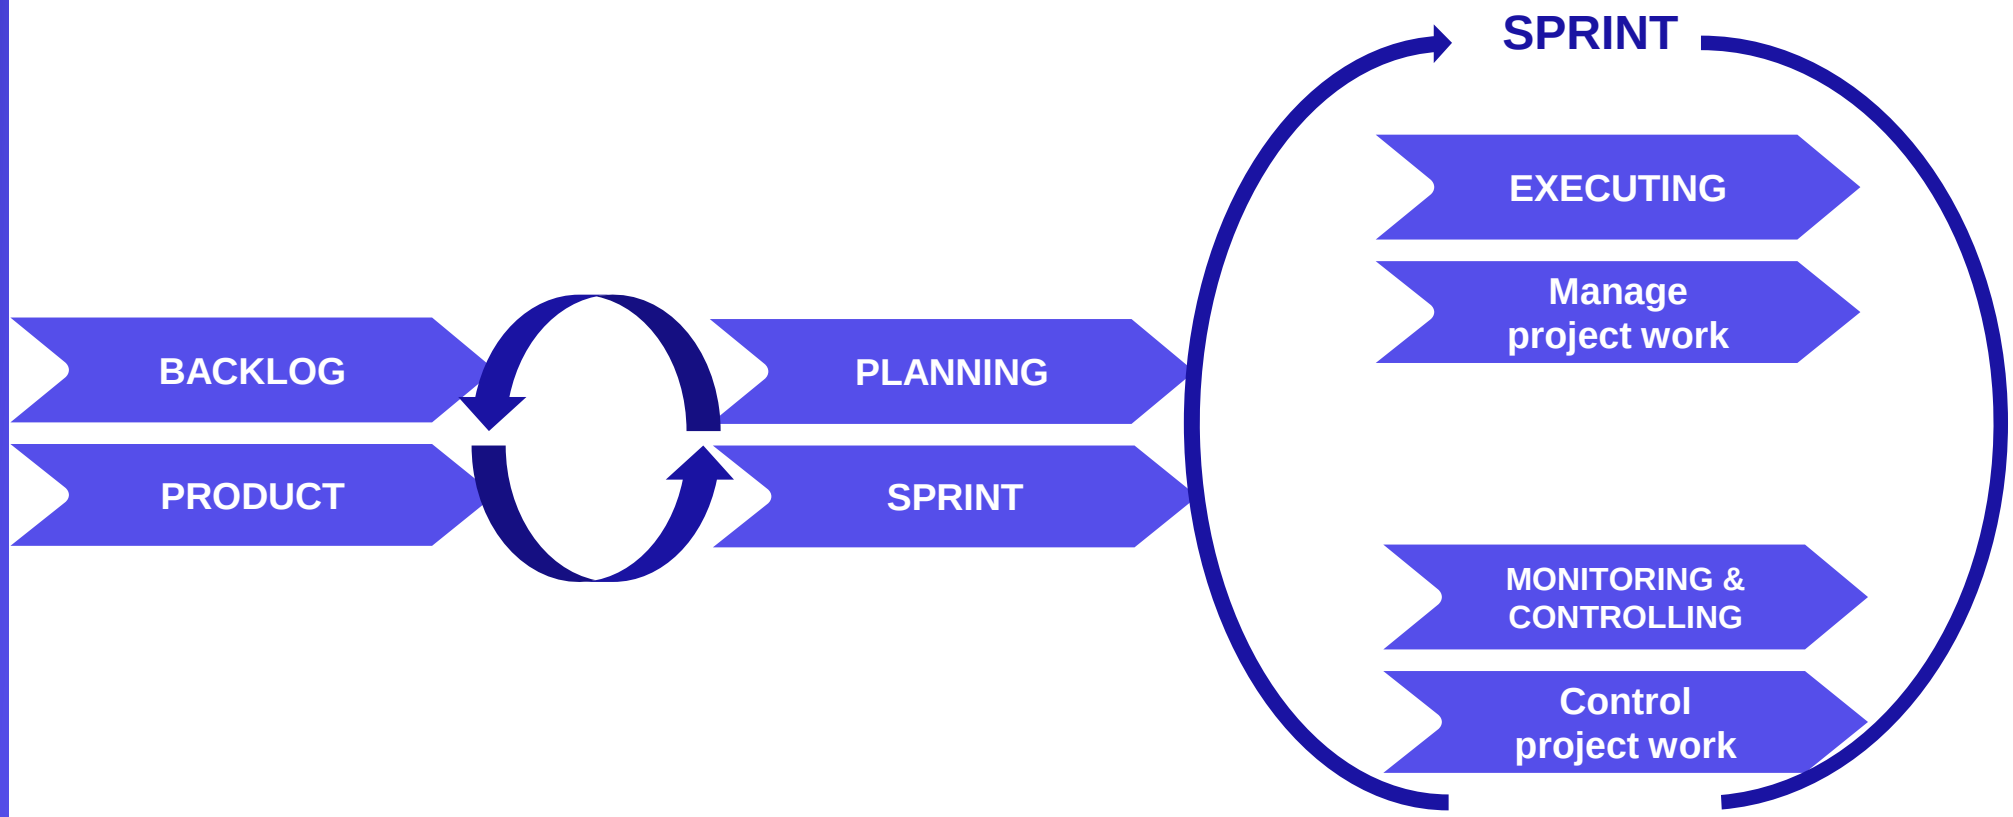


3. CYCLE DE VIE PROJET AGILE

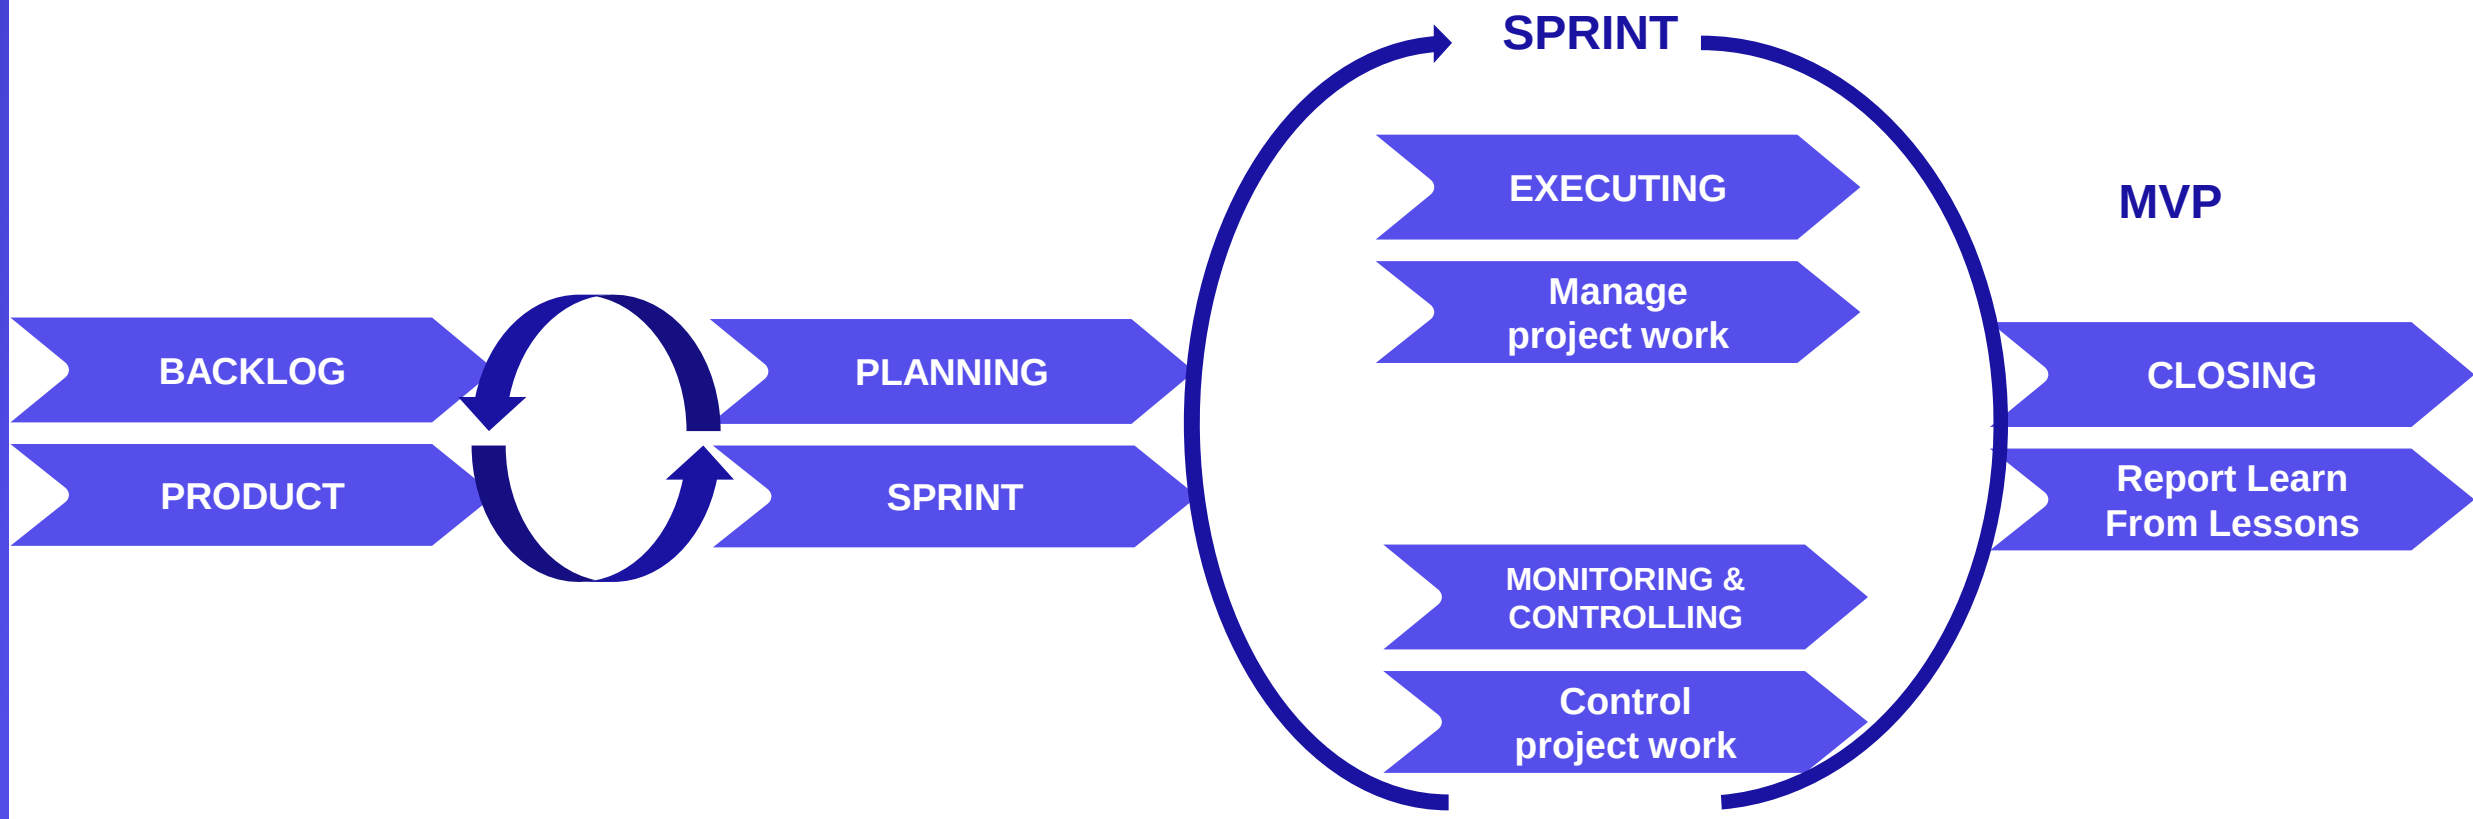

3. CYCLE DE VIE PROJET AGILE

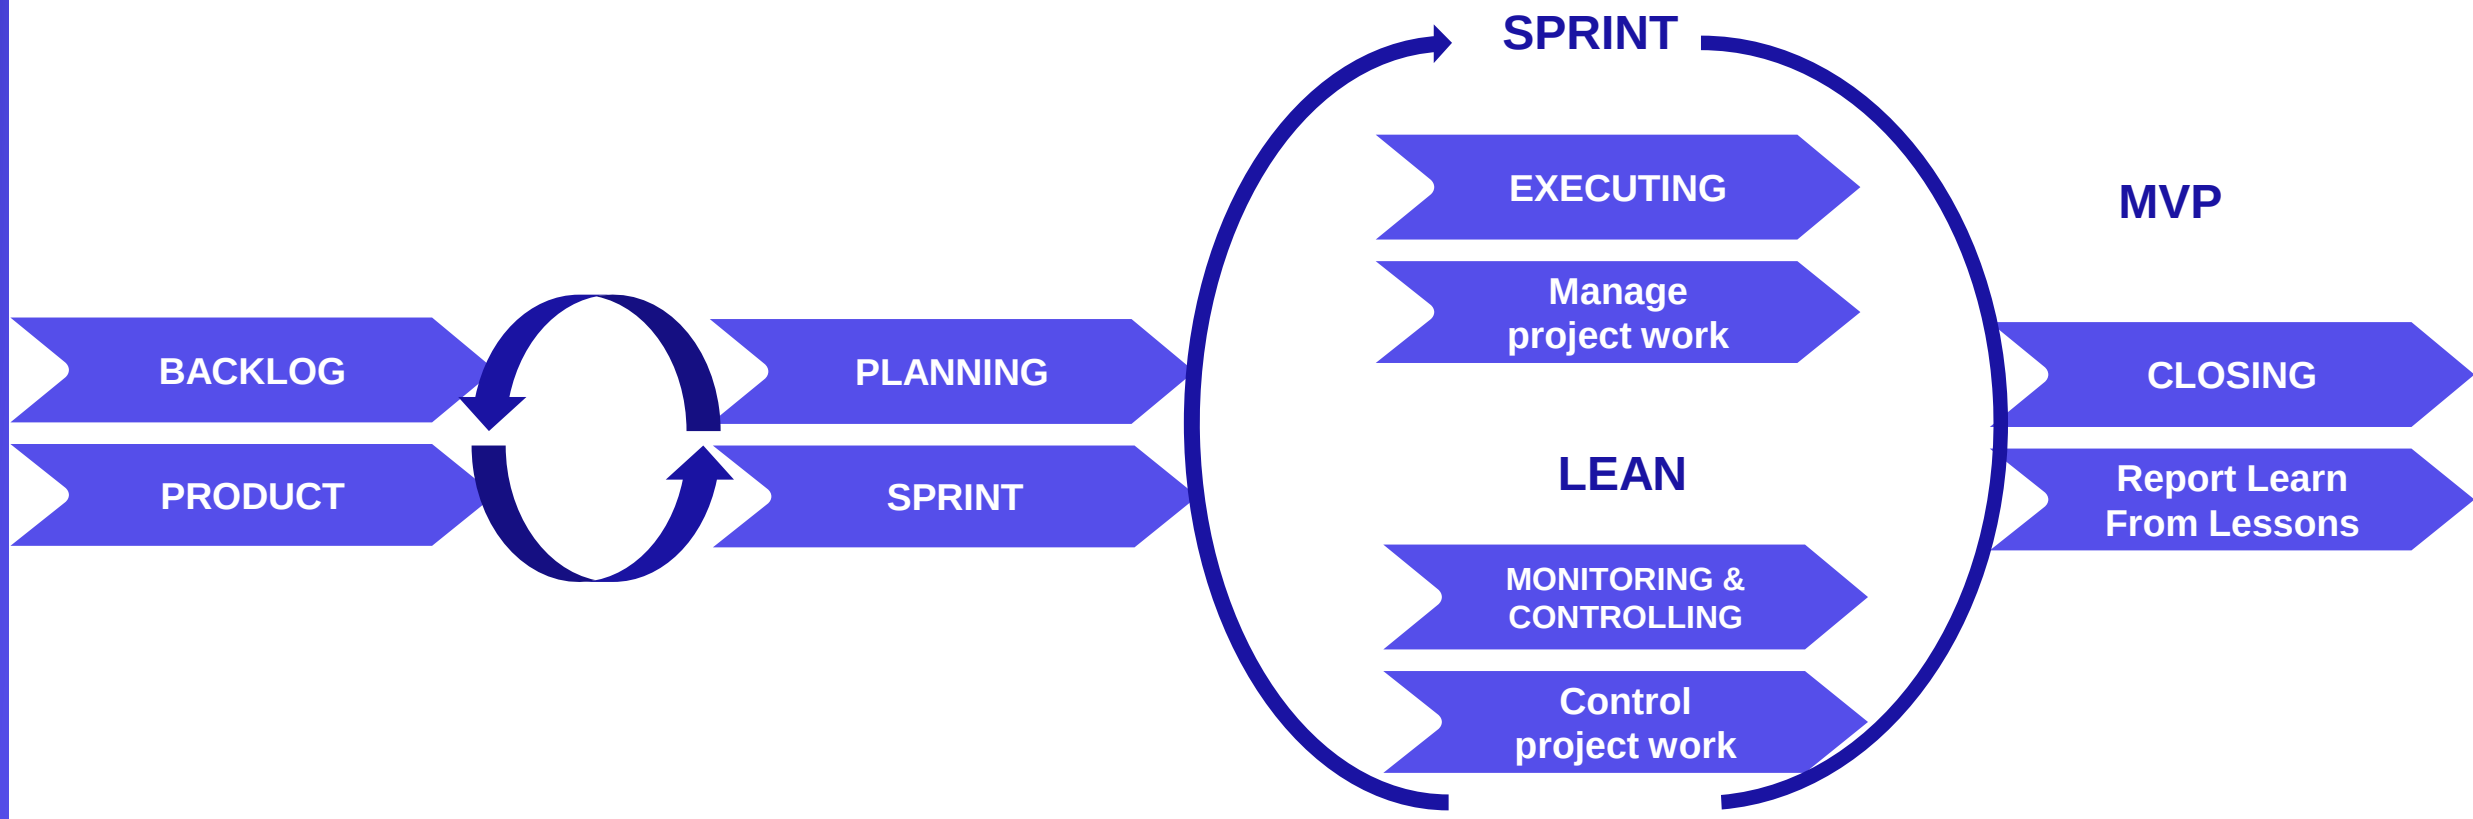

3. CYCLE DE VIE PROJET AGILE

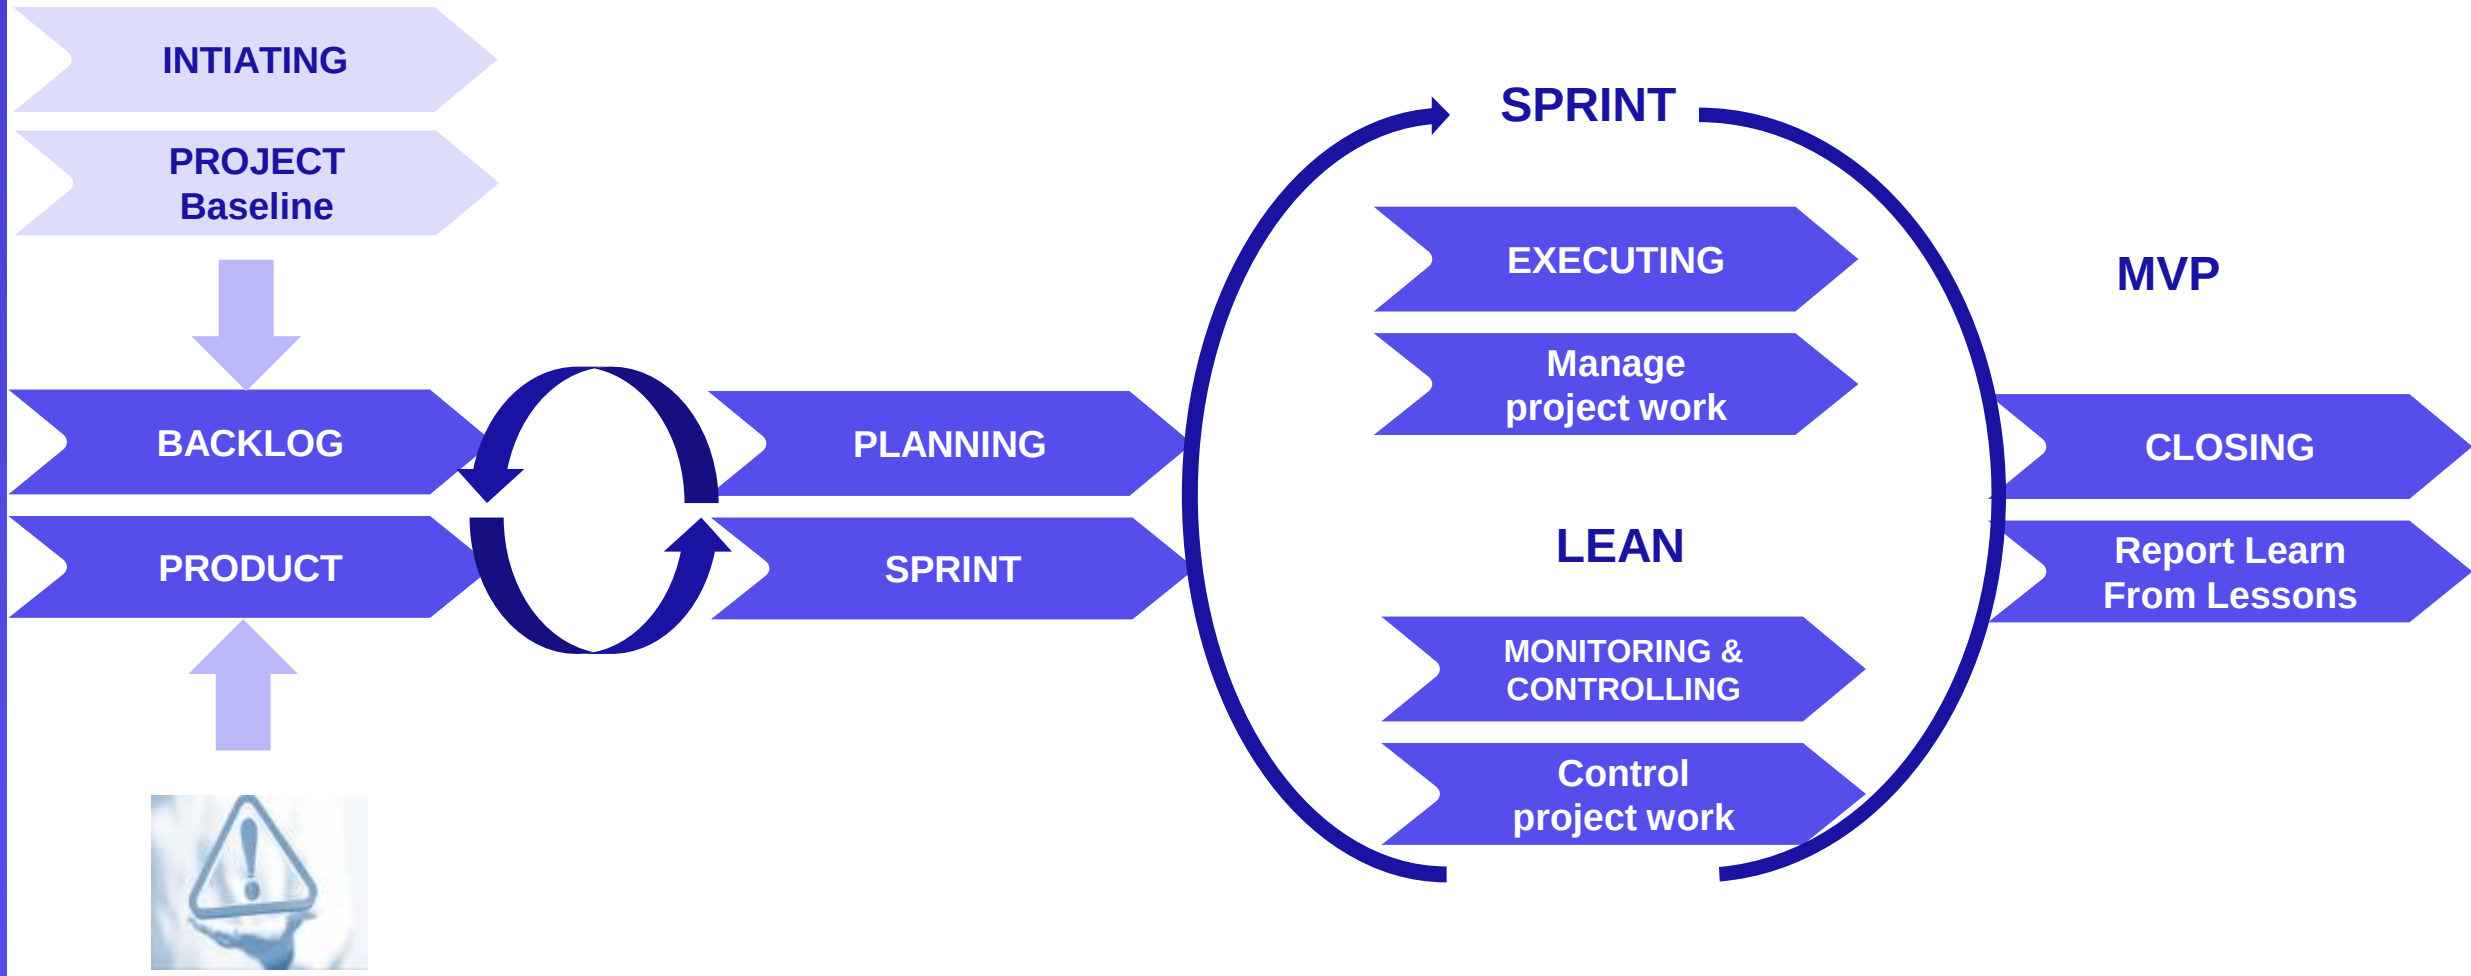

Date

4. LIVRABLES PROJET AGILE

Vs

PROJET PREDICTIF

Présenté par :

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF



4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF



1. Project Charter
2. Business Model
3. Business Case
4. Stakeholder

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF



- Change Management Plan
- Requirements – Scope (RTM)
- PBS – OBS – WBS
- Schedule Management Plan
- Estimate Costs - Budget
- Quality Management Plan
- HR Management Plan
- Risk Management Plan
- Risk Management Plan
- Communication Pan

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF



- Change Management Plan
- Requirements – Scope (RTM)
- PBS – OBS – WBS
- Schedule Management Plan
- Estimate Costs - Budget
- Quality Management Plan
- HR Management Plan
- Risk Management Plan
- Risk Management Plan
- Communication Pan

LE PROJECT MANAGEMENT PLAN

UN LIVRABLE ESSENTIEL AU SUCCES D'UN PROJET
(**80% des coûts sont engagés par le PMP**)

LA RESPONSABILITE DU PM EST FONDAMENTALE
(le PMP formalise l'intégration du Projet)

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF




- Project Charter
- Business Model
- Business Case
- Stakeholder

- Change Management Plan
- **Requirements – Scope (RTM)**
- **PBS – OBS – WBS**
- Schedule Management Plan
- Estimate Costs - Budget
- Quality Management Plan
- HR Management Plan
- Risk Management Plan
- Risk Management Plan
- Communication Pan

STRUCTURATION / PERIMETRE / VALEUR / COMPETITIVITE / PROFITABILITE

LA RESPONSABILITE DU PM EST FONDAMENTALE

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF

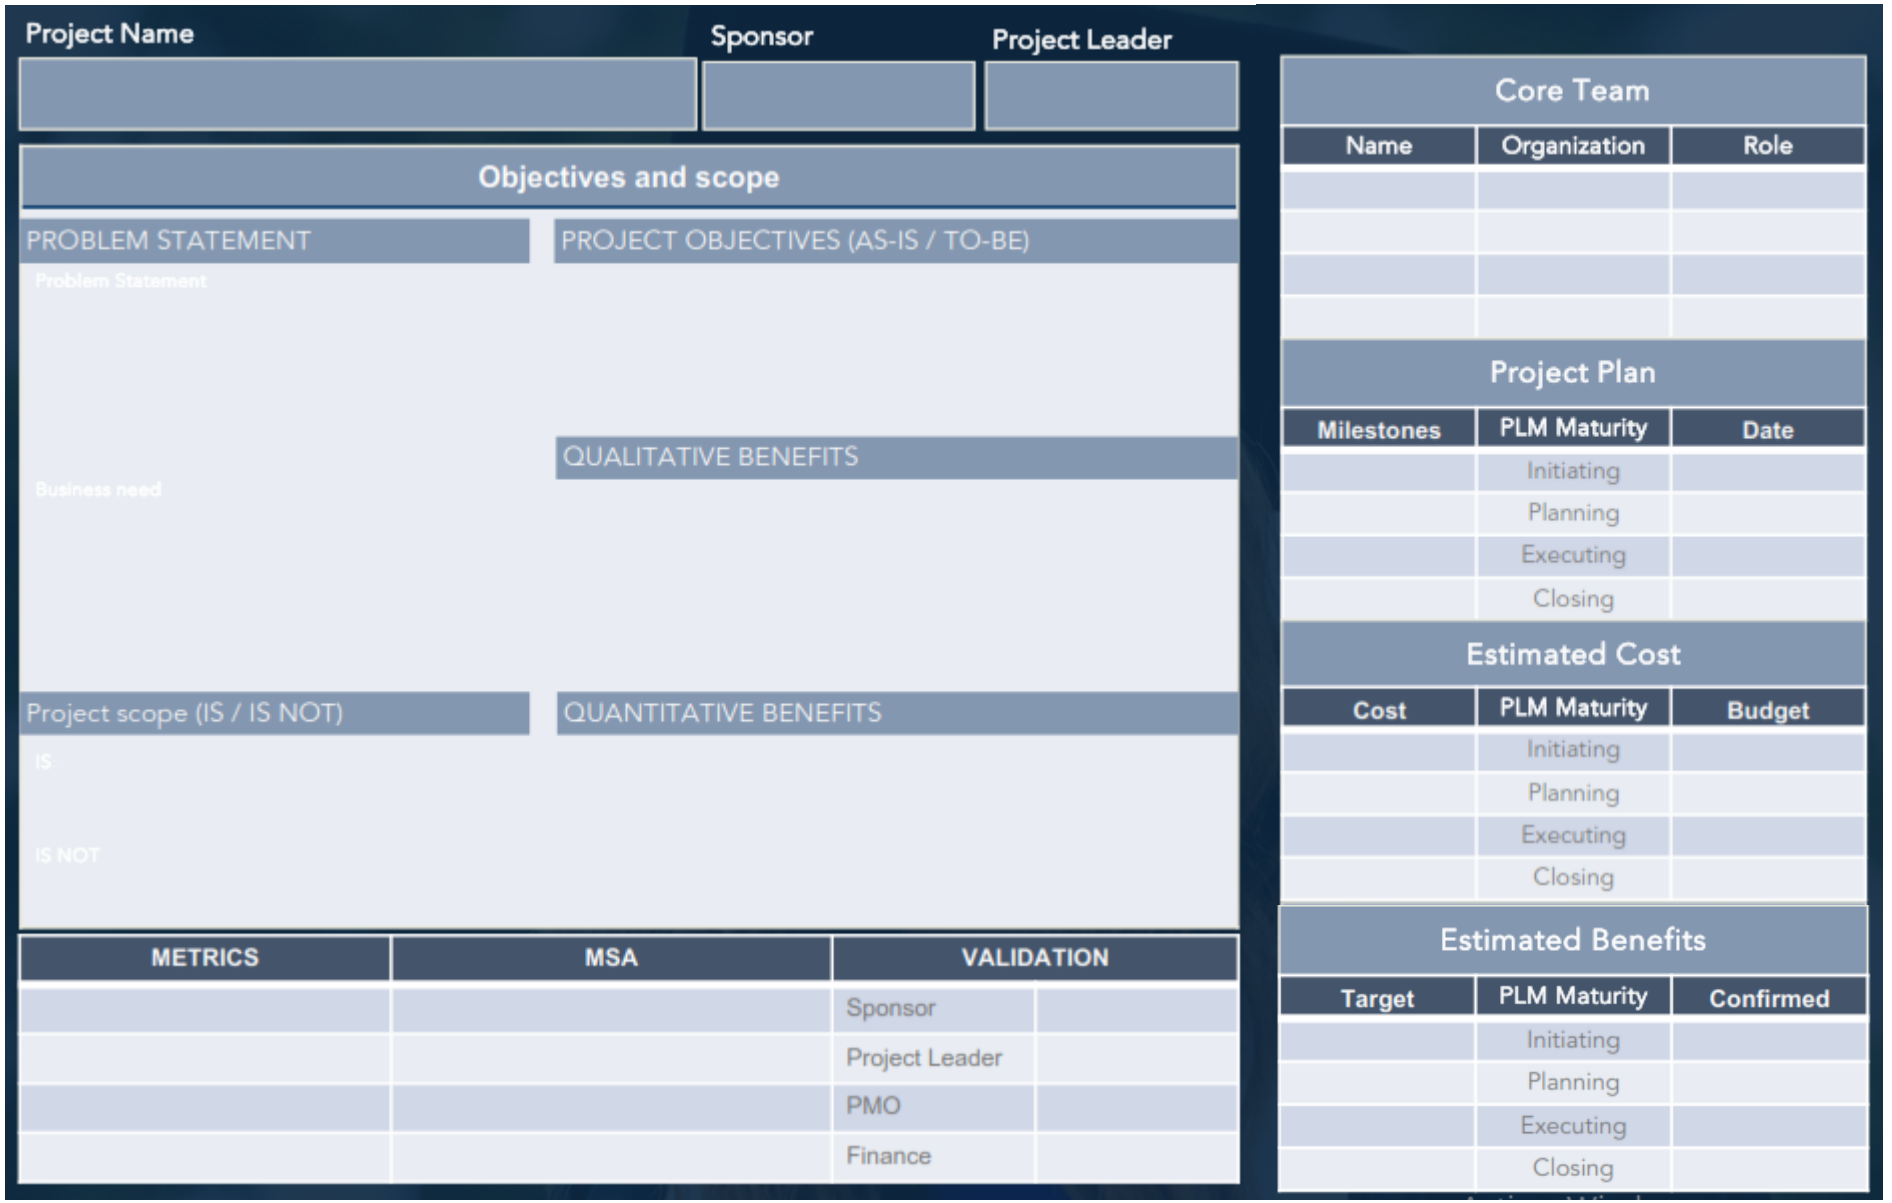

Project Name	Sponsor	Project Leader

Objectives and scope

PROBLEM STATEMENT	PROJECT OBJECTIVES (AS-IS / TO-BE)
Problem Statement	
Business need	QUALITATIVE BENEFITS
Project scope (IS / IS NOT)	QUANTITATIVE BENEFITS
IS	
IS NOT	

METRICS	MSA	VALIDATION	
		Sponsor	
		Project Leader	
		PMO	
		Finance	

Core Team

Name	Organization	Role

Project Plan

Milestones	PLM Maturity	Date
	Initiating	
	Planning	
	Executing	
	Closing	

Estimated Cost


Cost	PLM Maturity	Budget
	Initiating	
	Planning	
	Executing	
	Closing	

Estimated Benefits

Target	PLM Maturity	Confirmed
	Initiating	
	Planning	
	Executing	
	Closing	

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF

Université Ibn Tofaïl
Faculté des Sciences

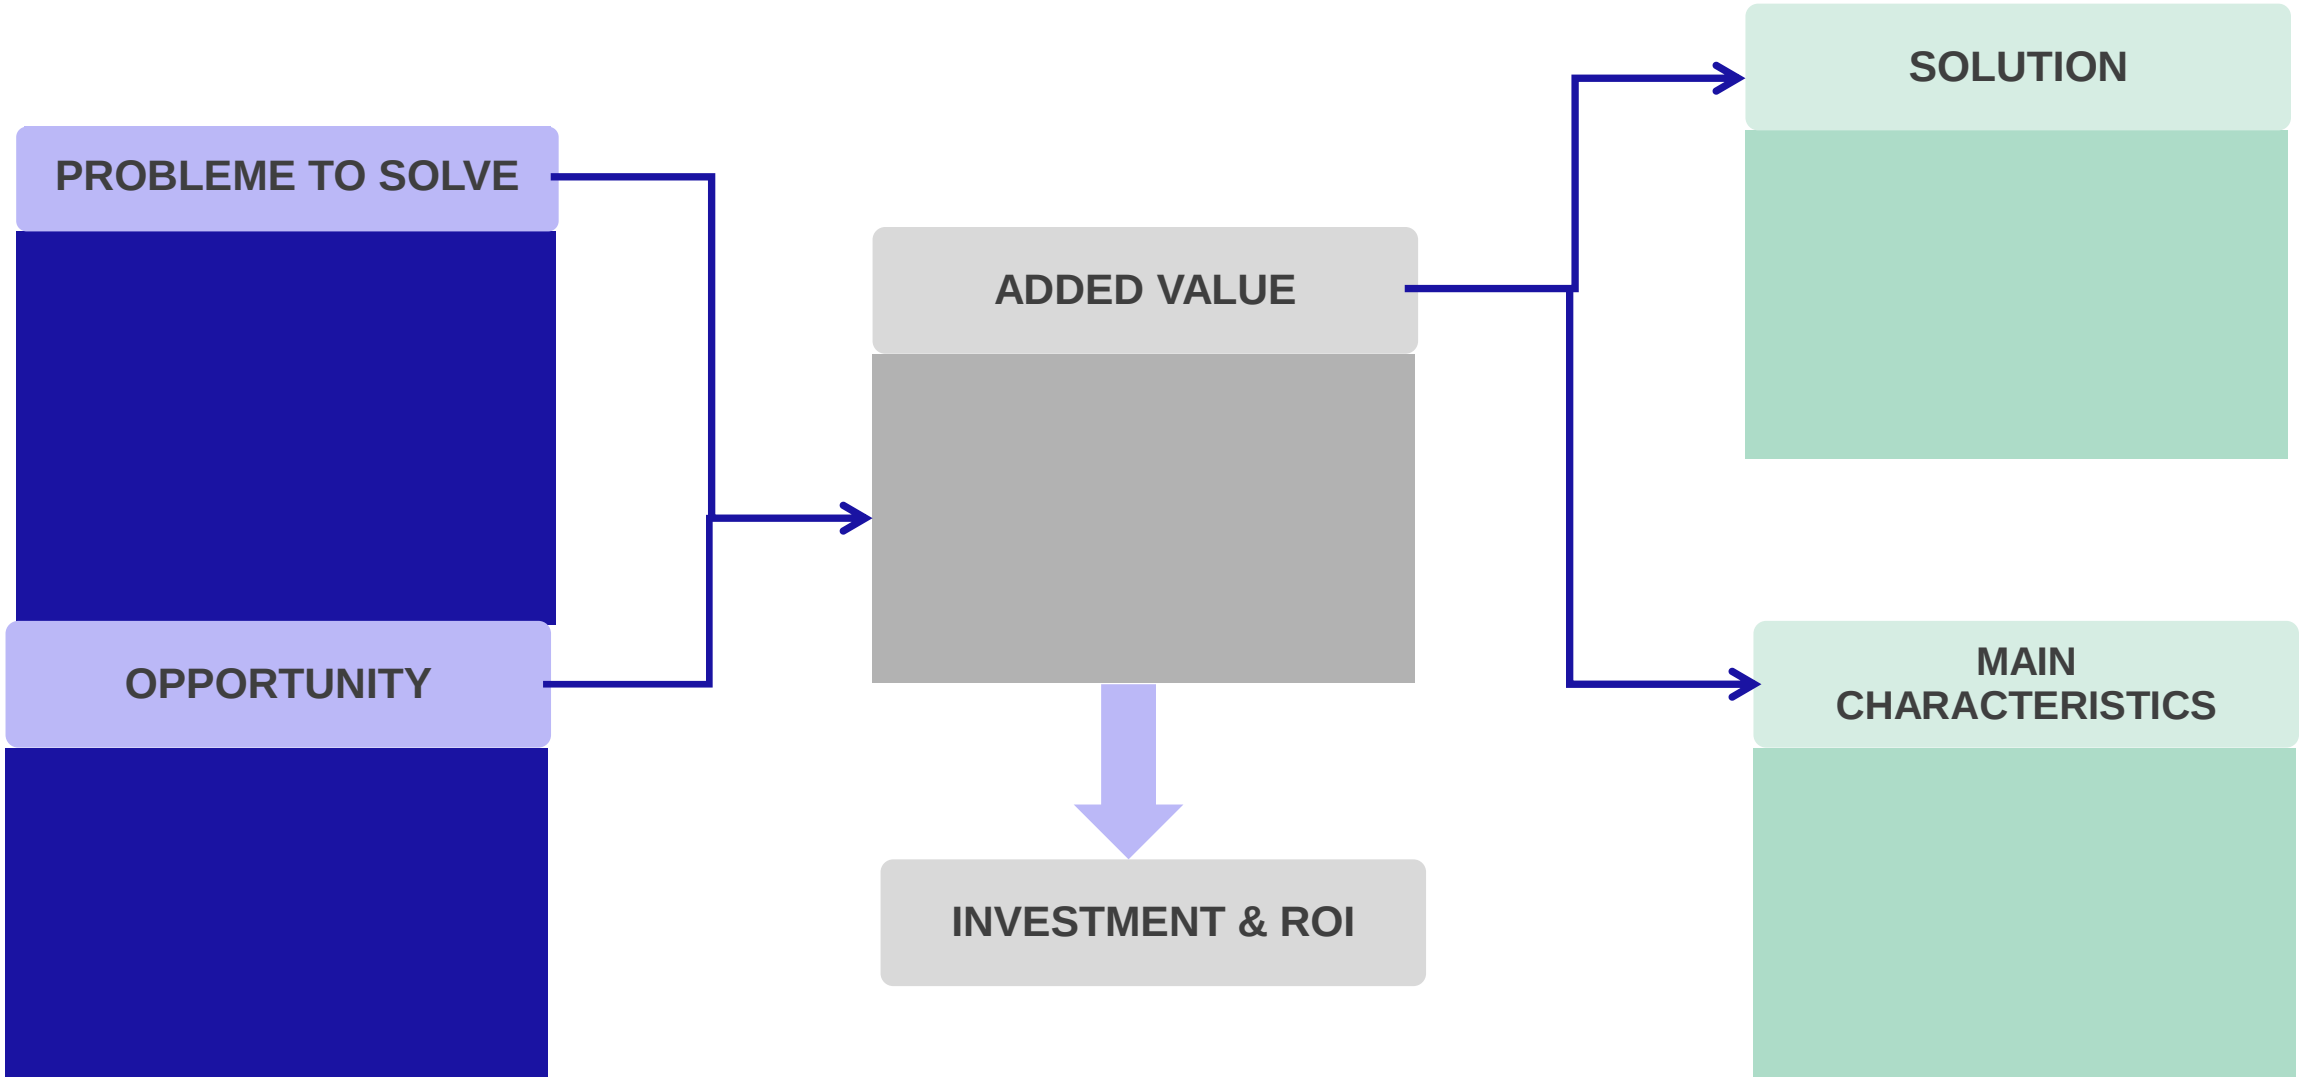


4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF

Université Ibn Tofail
Faculté des Sciences

REQUIREMENT TRACEABILITY MATRIX - RTM							
Project Name							
Project Description							
ID	Sub-ID	Requirement Description	Business & Customer Needs	Project Objectives	Project Activity	PLM	WBS
001	1.0						
	1.1						
	1.2						
002	2.0						
	2.1						
	2.2						
003	3.0						
	3.1						
	3.2						
004	4.0						
	4.1						
	4.2						
005	5.0						
	5.1						
	5.2						

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF

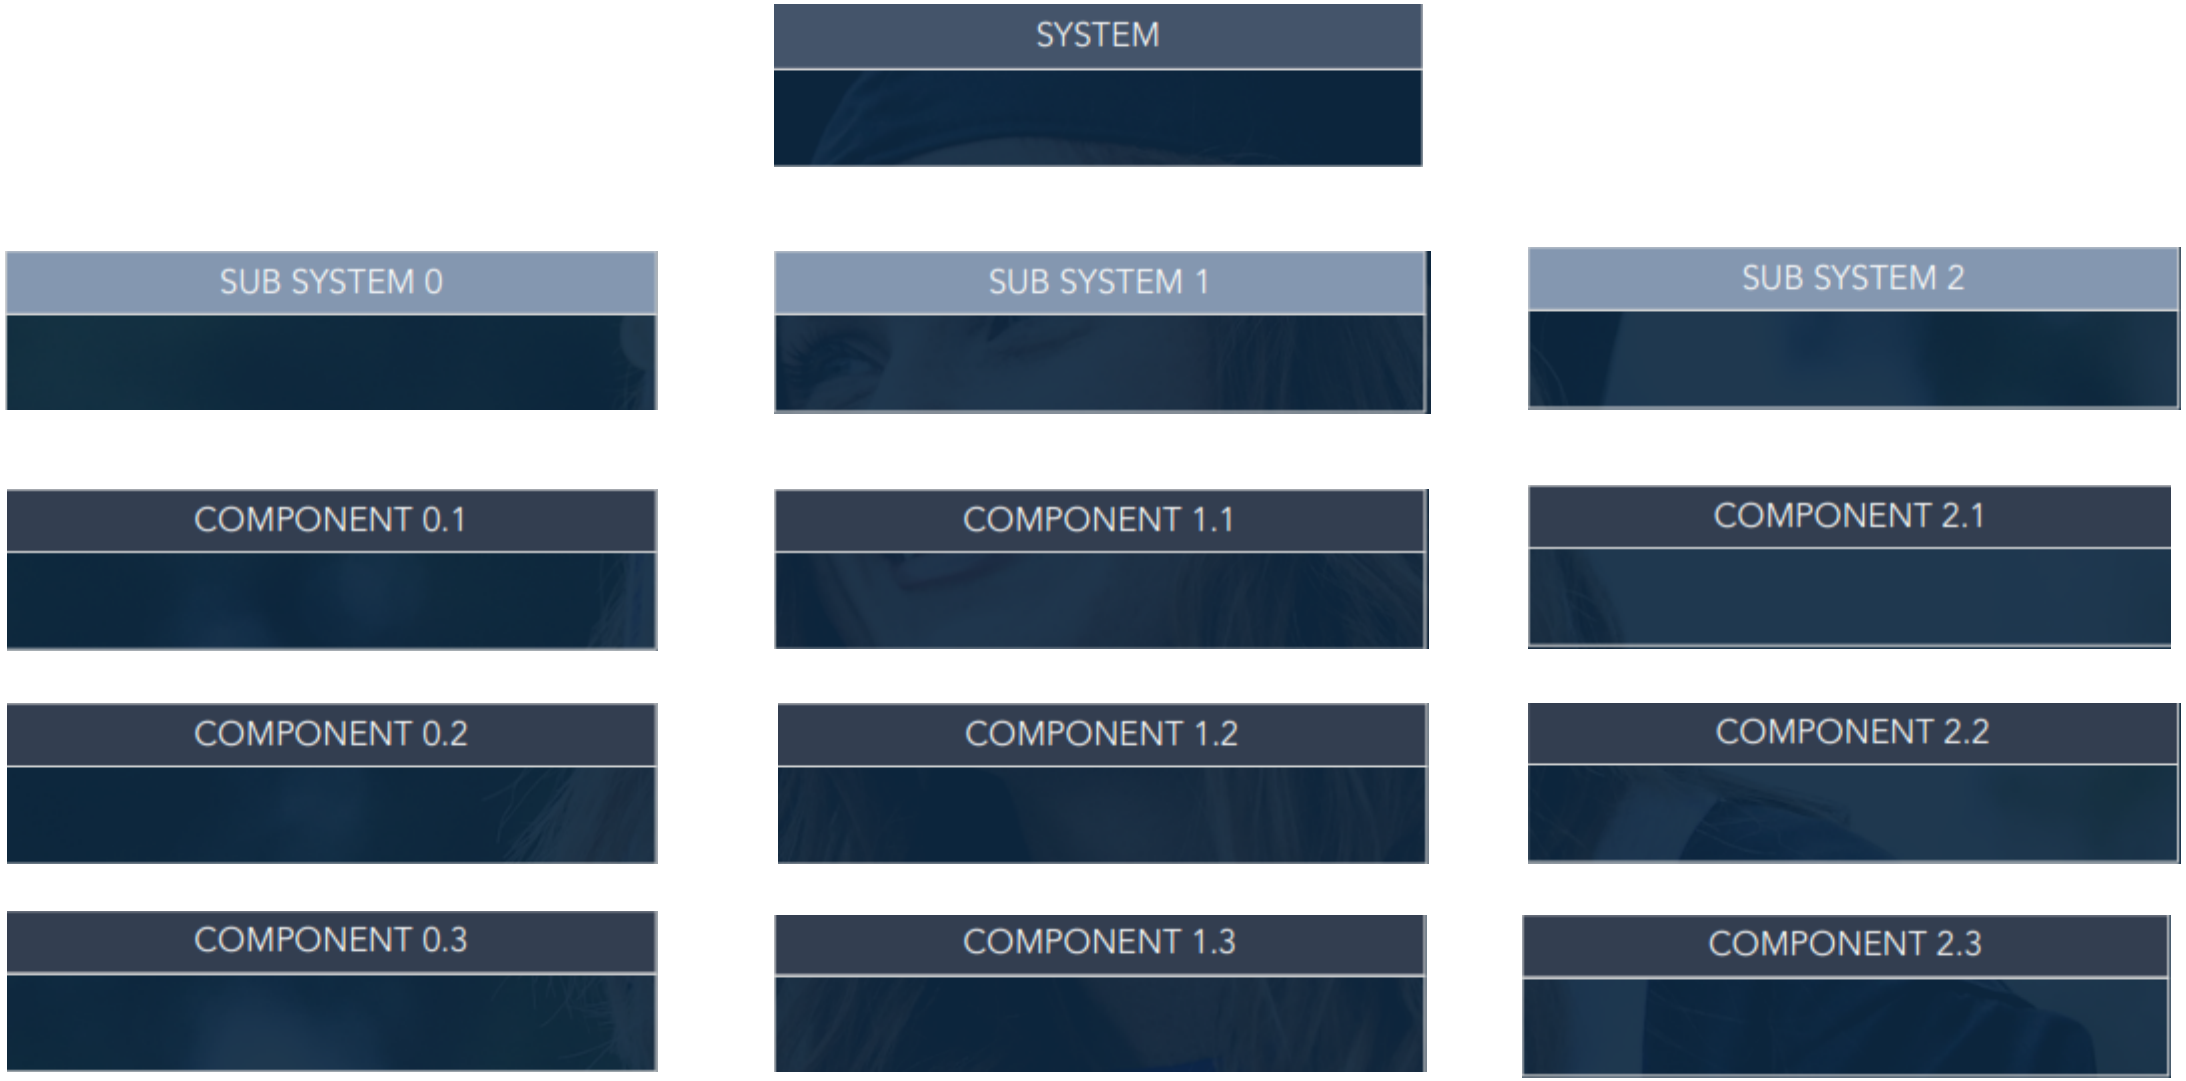

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF



4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF



4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF

Université Ibn Tofail
Faculté des Sciences



4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF

	PREDICTIF	AGILE
Project Charter	OUI	
Business Model - Case	OUI	
RTM - Requirement Traceability Matrix	OUI	PRODUCT BACKLOG
PBS (Product Breakdown Stucture)	OUI	PRODUCT BACKLOG
WBS (Work Breakdown Structure)	OUI	SPRINT BACKLOG
Performance Management (OTOCOQ)	OUI	SPRINT MANAGEMENT
Budget	OUI	SPRINT MANAGEMENT
Schedule - Roadmap	OUI	SPRINT PLANNING
Resources Management	OUI	SPRINT MANAGEMENT
Governance	OUI	SELF ORGANIZED
Communication - Training	OUI	SELF ORGANIZED
Change Management	OUI / NON	

4. LIVRABLES PROJET AGILE Vs PROJET PREDICTIF

Université Ibn Tofail
Faculté des Sciences

	PREDICTIF	AGILE
Project Charter	OUI	??
Business Model - Case	OUI	??
RTM - Requirement Traceability Matrix	OUI	PRODUCT BACKLOG
PBS (Product Breakdown Stucture)	OUI	PRODUCT BACKLOG
WBS (Work Breakdown Structure)	OUI	SPRINT BACKLOG
Performance Management (OTOCOQ)	OUI	SPRINT MANAGEMENT
Budget	OUI	SPRINT MANAGEMENT
Schedule - Roadmap	OUI	SPRINT PLANNING
Resources Management	OUI	SPRINT MANAGEMENT
Governance	OUI	SELF ORGANIZED
Communication - Training	OUI	SELF ORGANIZED
Change Management	OUI / NON	??

Date

5. CONCEPTS

Présenté par :

5. CONCEPTS

- Connected Cycles : Business / Product / Project
- Project / Program / Portfolio
- Project Management
- Program & Portfolio Management
- Organizational Project Management
- Operation VS Project
- PMO Project Management Office
- Organizational & Project Governance
- Organizational Structure
- OPA – Organizational Process Assets
- EEF – Enterprise Environmental Factor

BUSINESS / PRODUCT / PROJECT CONNECTED CYCLES

Université Ibn Tofail
Faculté des Sciences

Business lifecycle addresses the overall organizational trajectory while the product lifecycle hones in on specific offerings, and the project lifecycle pertains to temporary endeavors with defined goals in order to develop specific product or services.
Product lifecycle focuses on the journey of a specific product from development and introduction to market. Stages commonly include introduction, growth, maturity, and decline.
Project lifecycle is concerned with the phases a project passes through from initiation to completion. Common stages encompass initiation, planning, execution, monitoring/controlling, and closure.



Business Lifecycle encompasses Product & Project Lifecycles, Product Lifecycle encompasses Project Lifecycle.

PROJECT

Université Ibn Tofail
Faculté des Sciences


- Project => Always temporary, create something unique (product or service)
- Why to initiate Project => Response to Market, customer or business need
- Project => Always provide business **value**
- Project => Impact positively organizations



PROGRAM & PORTFOLIO

Université Ibn Tofail
Faculté des Sciences


- **Program** => Group of related **projects** contributing to the same goal
- **Portfolio** => Group of related **programs** contributing to the same strategy
- **Portfolio** => Can be composed of all categories contributing to a same strategy
  - **Programs**
  - **Projects**
  - Necessary related **operations**

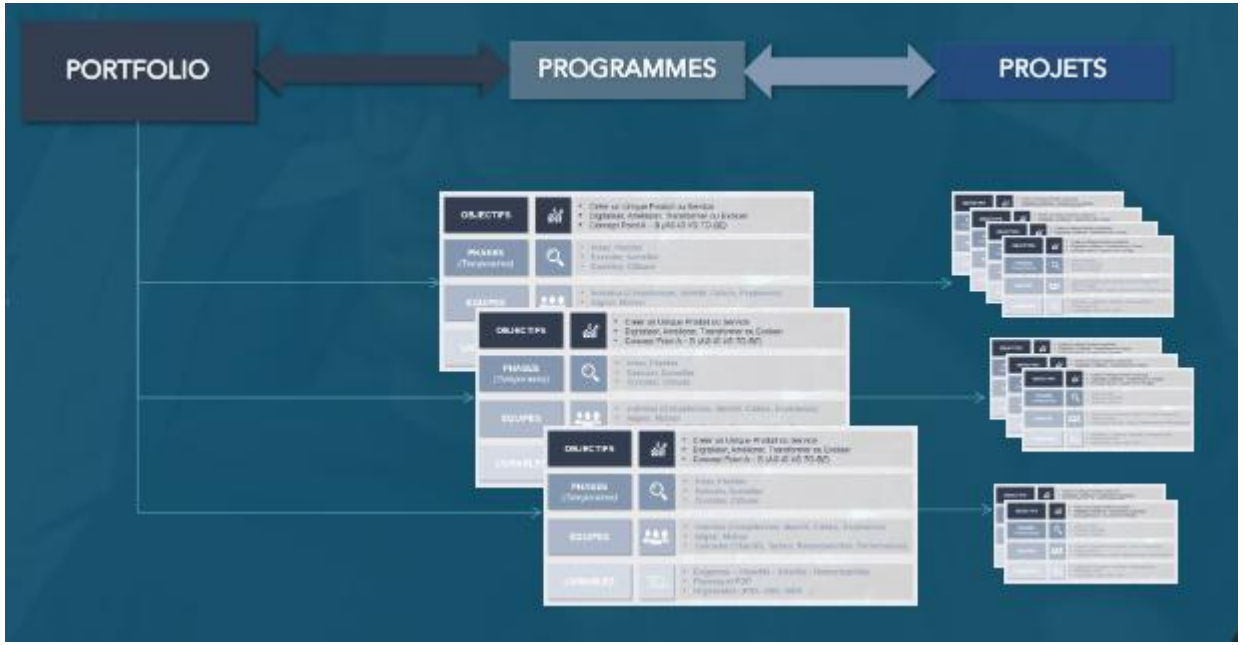

PREDICTIVE PROJECT MANAGEMENT

Université Ibn Tofail
Faculté des Sciences

- Project => Have requirements to meet like :
  - Scope, Budget, Time, Quality, Laws & Standards…
  - Quality, Customer Satisfaction
  - Value creation & performance (efficiency / effectiveness)
- Project Management => Use of Specific Processes, Tools & Techniques to succeed
- Project Management => 49 Standard Processes involving multiple Tools & Techniques
- Project Management => 5 Process Groups + 10 Knowledge Areas

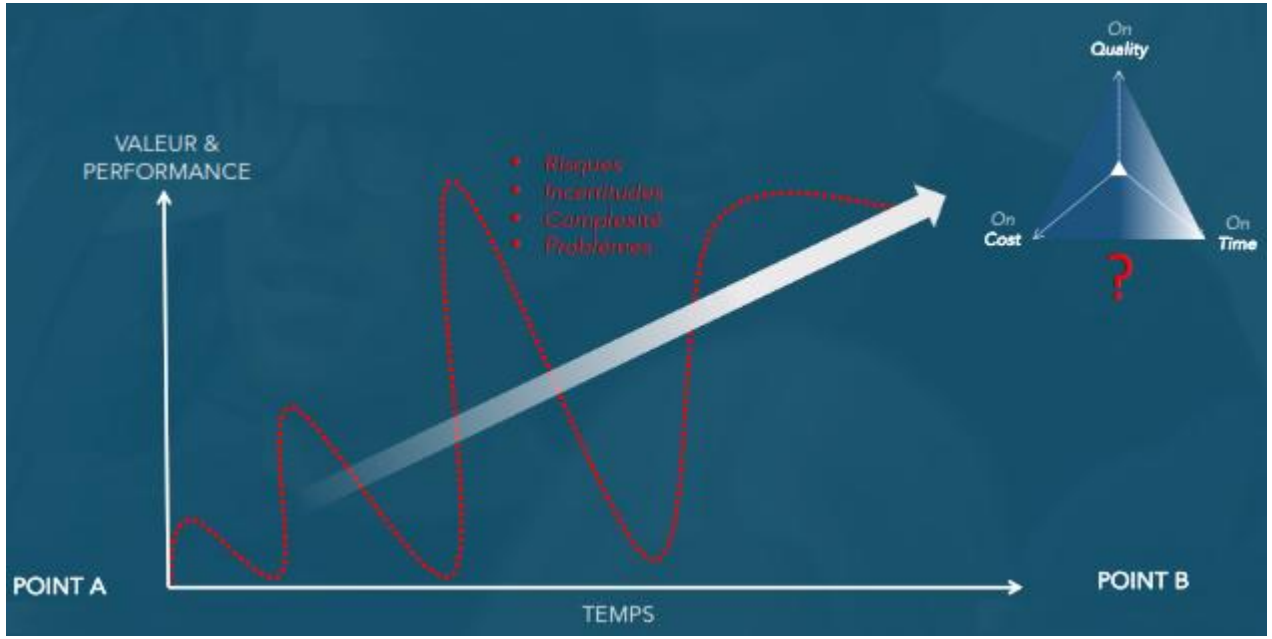


PROGRAM & PORTFOLIO MANAGEMENT

Université Ibn Tofail
Faculté des Sciences

Program Management => Coordination of all related projects
Program Management => Allow resources optimisation
Program Management => Allow better priority / urgency prioritisation
Program Management => Allow better conflicts management
Program Management => Program level is necessary only if it brings value
Portfolio Management => Portfolio level is necessary only if it brings value
Portfolio Management => Can sometimes replace program management

Niveau	**Exemple concret**	**Objectif stratégique**
Portefeuille	Transformation numérique de l'université	Modernisation globale
Programme	Digitalisation des services étudiants	Automatiser inscriptions, stages, tableaux de bord
Projets	Application Web Universitaire, GED, Portail RH	Produits concrets livrables

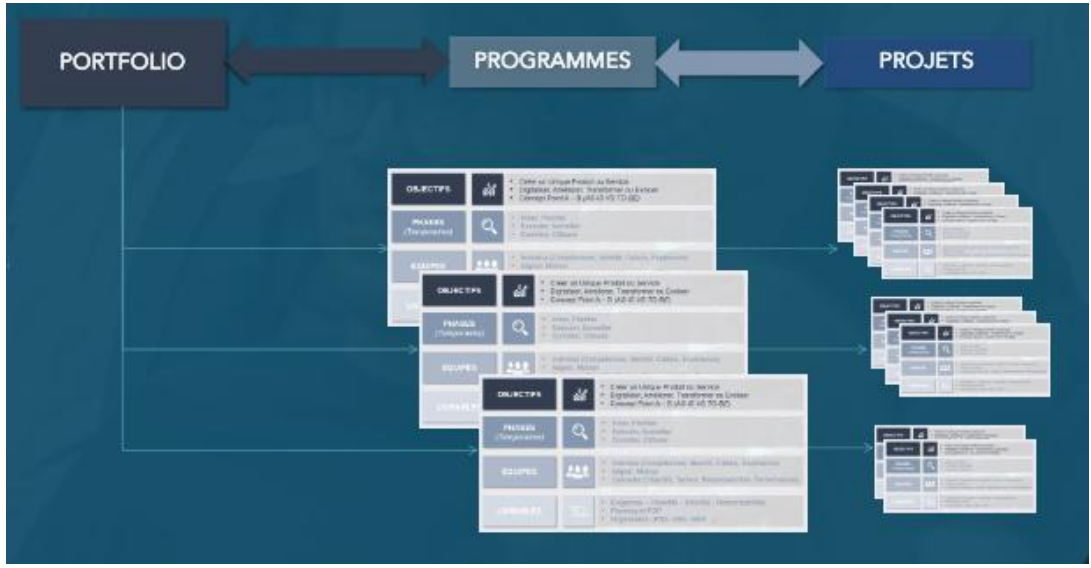

OPM - ORGANIZATIONAL PROJECT MANAGEMENT

Université Ibn Tofail
Faculté des Sciences

Organizational Project Management (OPM) est une **approche systématique** qui permet à une organisation d'**aligner ses projets, programmes et portefeuilles sur sa stratégie globale**, afin de **maximiser la performance et la création de valeur**.

OPM => Organizational Project Management
OPM => Provide guidance to company strategy
OPM => Define company strategic framework
OPM => Define Portfolio, Program, Project Management
OPM => Define all works to achieve strategic goals

STRATÉGIE ORGANISATIONNELLE
↓
PORTFOLIO MANAGEMENT
↓
PROGRAM MANAGEMENT
↓
PROJECT MANAGEMENT



Company Strategy Framework


OPERATION VS PROJECT

Université Ibn Tofail
Faculté des Sciences

Opération : sans fin c'est continu. **Projet** c'est temporaire (limiter dans le temps càd début et fin)

- Operation => Can be a strategic company function led by COO **or a process**
- Operational Process => Is an ongoing process (**not temporary**)
- Operational Process => produce **same** product / service many times
- Project => Is **always temporary** (main difference with operation)
- Project & Operation => Can be connected and one can come after the other
- Project & Operation => Can be connected and combined
- Portfolio => Is composed of project & programs + related operations

Niveau	Exemple	Type d'opération
Fonction stratégique	Direction des opérations de l'université (pilotée par le Vice-Doyen ou COO)	Supervision globale de la gestion académique, financière et logistique
Processus opérationnel	Traitement des inscriptions étudiantes, génération des bulletins, maintenance des serveurs	Activités répétitives assurant la continuité du service

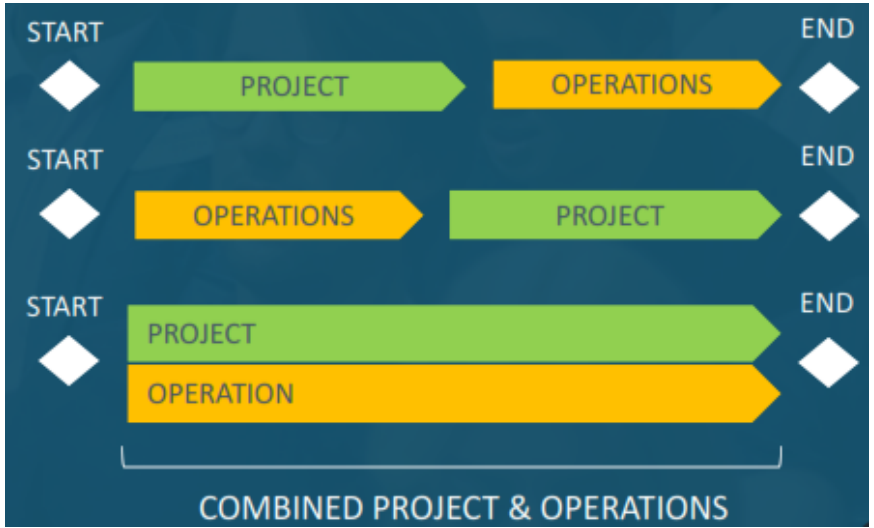

PMO – PROJECT MANAGEMENT OFFICE

Université Ibn Tofail
Faculté des Sciences

Le **PMO (Project Management Office)** est une **structure organisationnelle** qui **standardise les processus de gestion de projet** et facilite le **partage de ressources, de méthodologies, d'outils et de bonnes pratiques** à travers les projets.


- **PMO** => provides, shares & maintains standards & procedure
- **PMO** => A project organization always considers PMO
- **PMO** => Categorized into 3 groups : Supportive, Controlling, Directive
  - **Supportive** PMO => Support project (has **no control**)
  - **Controlling** PMO => Has control on the project (**don't make** direct **decisions**)
  - **Directive** PMO => Manage projects among organization (**make** direct **decisions**)
  - **Authority levels** :
    - Supportive PMO => Low
    - Controlling PMO => Moderate
    - Directive PMO => High



PMO – PROJECT MANAGEMENT OFFICE

Exemple de PMO Universitaire
Contexte : Université souhaitant moderniser ses systèmes numériques.
PMO Universitaire – "Transformation Digitale"

Projet	Chef de projet	Rôle du PMO
Application Web Universitaire	Pr. Amnai	Standardisation du plan projet et suivi qualité
Portail RH Enseignants	DSI	Contrôle du budget et du planning
Système GED Rectorat	Service IT	Reporting mensuel au comité de pilotage
Smart Campus (IoT)	Cellule technique	Coordination inter-départements

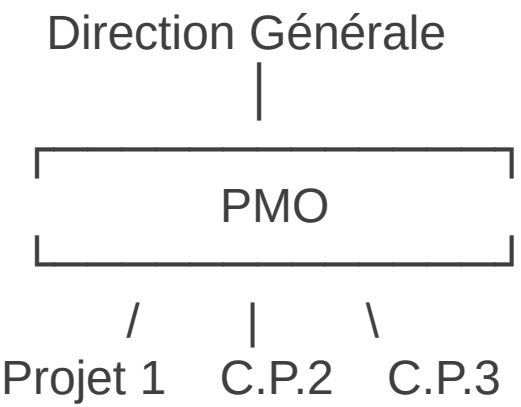

Le **PMO** agit comme **interface entre la stratégie (direction)** et **l'exécution (chefs de projets)**.

Le PMO universitaire :

- Met en place des **indicateurs de performance (KPI)** : taux de livraison, écarts planning, qualité du code.
- Fournit des **modèles standardisés** : charte projet, PAQ, registre des risques.
- Anime les **comités de pilotage**.
- Assure la **formation continue des chefs de projets**.

ORGANIZATIONAL & PROJECT GOVERNANCE, ORGANIZATIONAL STRUCTURE

Université Ibn Tofaïl
Faculté des Sciences

•Elles définissent **comment une organisation prend ses décisions**, **comment elle est structurée**, et **comment un projet est contrôlé et orienté** à l'intérieur de ce cadre.

•Organizational Governance => High level goals, roadmaps, procedures…
•Organizational Governance => Allow that work are executed with compliance
•Organizational Structure => Organic (simple), Functional, Multidivisional, Matrix (weak, balanced, strong), PMO, Project Oriented and others like : Virtual, Hybrid…
•Organizational Structure => **3 Majors Structures : Functional, Matrix & Project**
•Project Governance => Provides project team with policies & processes
•Project Governance => Provides project team "right" decision making
•Project Governance => Provides project team models, techniques & tools



ORGANIZATIONAL & PROJECT GOVERNANCE, ORGANIZATIONAL STRUCTURE

Université Ibn Tofail
Faculté des Sciences

[ORGANIZATIONAL GOVERNANCE]

↳ définit les règles, la stratégie et la conformité globales

↓

[ORGANIZATIONAL STRUCTURE]

↳ détermine comment les rôles et les responsabilités sont organisés

↓

[PROJECT GOVERNANCE]

↳ applique ces principes à un projet spécifique



OPA – ORGANIZATIONAL PROCESS ASSETS

Université Ibn Tofail
Faculté des Sciences

Organizational Process Assets (OPA) (les atouts de l'organisation) désigne **l'ensemble des plans, processus, politiques, procédures et bases de connaissances internes** à une organisation, qui influencent la **gestion et la réussite d'un projet**.

- OPA => Organizational Process Assets
- OPA => Is an important input for most of project management processes
- OPA => Formalize historical data & information for project management
- OPA frequently used are :
  - Risk Matrix
  - Project Guidelines
  - WBS (work breakdown structure) templates
  - Traceability matrix
  - Work Instructions….

OPA Examples



EEF – ENTERPRISE ENVIRONMENTAL FACTORS

Université Ibn Tofail
Faculté des Sciences

- EEF => Enterprise Environmental **Factors**
- EEF => Is an important input for most of project management processes
- EEF => Factors influencing companies, organizations & projects
- EEF => 2 types : can be **external** or **internal** to organizations

- EEF **Internal Factor** frequently used are :
  - Company culture & geography location
  - Company structure…

- EEF **External Factor** frequently used :
  - Governmental **Laws**
  - **Quality** & Safety **Standards**….

OPA = Ce que l'organisation a appris et documenté.
EF = Ce à quoi l'organisation doit s'adapter.

EEF Types

